

READ ME FIRST

About this sample

This page sets the scene for the sample. It appears only because this is an illustration. In a client engagement it would not be included unless the client specifically asked for it.

WHAT THIS IS

An example of the output the ENOS 360° Health Check produces.

Northwind Water and “Programme Meridian” are fictional - a smart-metering rollout with a new customer platform, at the end of definition, with the board about to be asked to release the build budget.

THE UNDERLYING REALITY (a well-run programme with three small gaps)

- A single, named, engaged SR0; a clear strategic anchor; scope and requirements in good order; a stable, motivated team. The basics are done well.
- Gap 1 - the benefits read well as narrative but are not yet measurable, baselined or owned, so the return cannot yet be stated in numbers.
- Gap 2 - business readiness is thin: no change-impact assessment, no adoption plan, and the operational teams have barely been engaged.
- Gap 3 - one honest divergence: the Technical Lead is more cautious than the Sponsor on whether the build estimate will hold. A flag, not a fault line.

© 2026 ENOS Limited. All Rights Reserved. Licensed under CC BY-NC-ND 4.0: download and share with full attribution; do not alter, build upon, or use commercially.

WHY IT LOOKS REAL

This presentation is an illustrative example of the ENOS assessment method applied to this scenario. From the next slide onward, this is the deck as clients receive it.

Programme Meridian

An independent assessment

Prepared for Northwind Water by ENOS Limited · June 2026

For: Helen Sample, Head of PMO

Independent assurance for the board ahead of the Gate to Build decision on 14 July.

A programme that is ready to fund

We interviewed four role-holders against the 360 question bank, recording 559 answers in total. The four views sit close together:

EXECUTIVE SPONSOR

79 %

PROGRAMME DIRECTOR

76 %

TECHNICAL LEAD

70 %

LEAD BUSINESS ANALYST


66 %

- A **13-point spread** separates the most and least confident role - the people who hold the programme broadly agree.
- A confident director should read this and feel confirmed, not exposed; the check stands behind the story with independent evidence.

BLENDED VIEW

74 %

Where Meridian stands today (blended view)

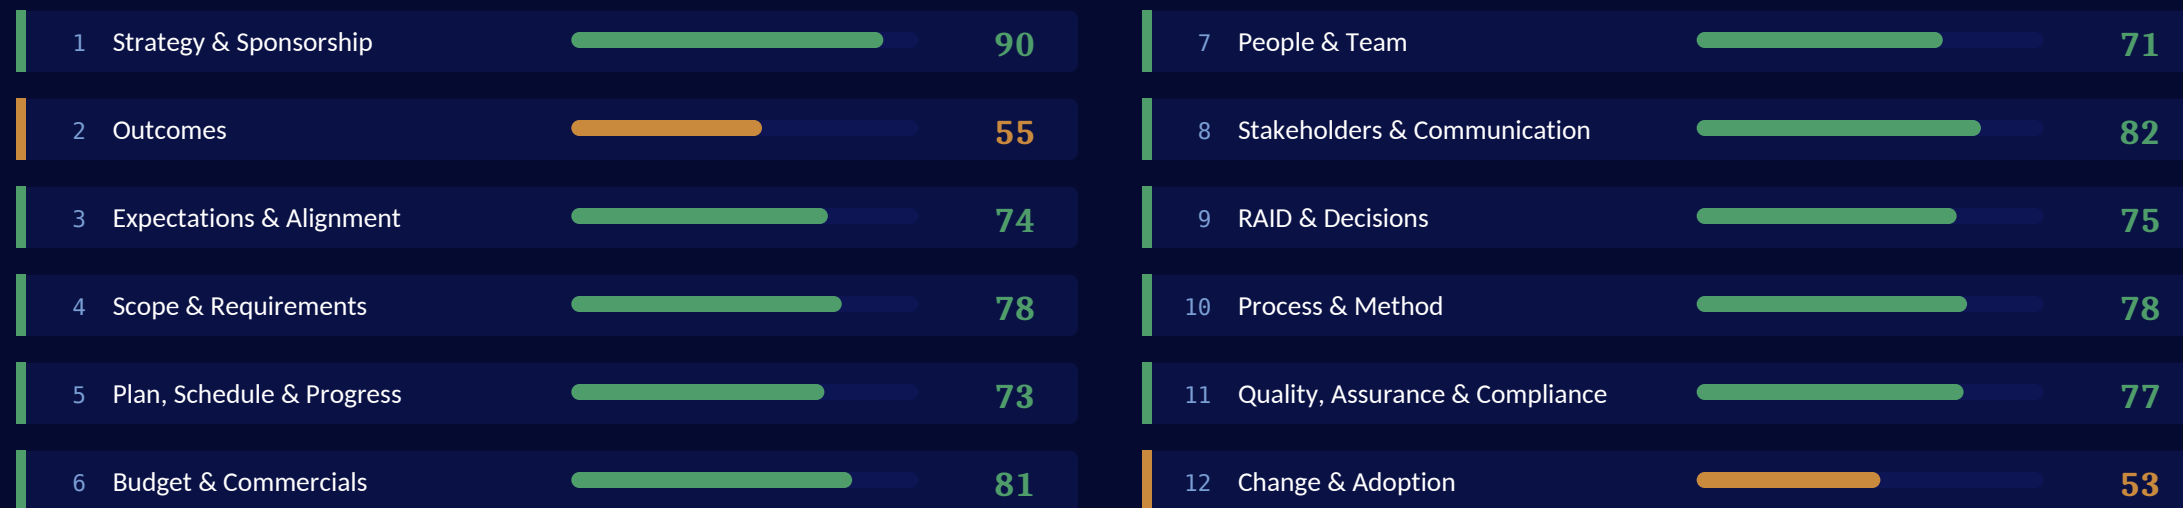

Ten of twelve areas sit in green. Two land in amber - and they are the point of the exercise: Outcomes (55) and Change & Adoption (53).

No area is red. These are gaps a strong team carries without noticing, because the work that closes them naturally comes later.

Three things worth fixing first

Outcomes - the benefits read well but cannot yet be measured: 66 vs 34

The Sponsor backs the business case (66); the Lead Business Analyst, closest to it, scores Outcomes at 34. The benefits are real but narrative, not numbers - no baselines, no targets, no named owner. Quantify and assign them before the gate.

Change & Adoption - readiness is thin, and that is normal, which is the trap

At 53, the lowest area on the board. The operational teams who will run the new platform have barely been engaged; there is no change-impact assessment and no adoption plan. Commission it now so adoption is built in, not bolted on.

Plan & Schedule - an honest difference on whether the estimate will hold

Green at 73, but it carries the one real difference of opinion. The Sponsor reads the build schedule as realistic (82); the Technical Lead, closest to the estimate, is more cautious (55). A flag, not a fault line - re-baseline the estimate bottom-up at mobilisation.

Where all four align - strong, settled foundations

Strategy & Sponsorship, Scope, Budget and Stakeholders all score in the high 70s to low 90s across every role. The board can take the foundations as settled and spend its attention on the few things that are not.

Proceed to approval, subject to three conditions

The evidence supports funding the build - with three conditions closed before or as part of the gate:

- 1 Quantify and own the benefits** convert the narrative benefits into baselined, measurable targets with a named owner.
- 2 Commission the change-impact and adoption work now** engage the operational teams and build readiness in, rather than bolting it on during build.
- 3 Re-baseline the build estimate bottom-up** firm the schedule against technical effort at mobilisation, so the date can be relied on.

Closing these conditions gives the board a single, independent line of sight on Programme Meridian ahead of the Gate to Build on 14 July.

This summary shows the headline. The complete 360° Health Check - all 12 areas, 54 sub-areas, 559 scored responses and the full role-by-role detail - is available in the full report.
